Executive One-Pager

Employee Onboarding Dashboard

A centralised onboarding portal with AI task drafting and complete progress visibility.

WHY

New joinees currently navigate onboarding through fragmented emails, ad-hoc Slack messages, and verbal instructions with no central system of record. Managers rebuild task lists from scratch for every hire, leading to inconsistent ramp-up times and missed compliance certifications. IT and HR spend unnecessary time answering repetitive access questions, while leadership lacks visibility into new hire progress.

WHAT WE WILL DELIVER

1. A dual-role web portal (Manager and New Joinee) providing automated AI-assisted task drafting, manual plan customization, certification tracking, and progress dashboards.
2. A searchable static Information Hub providing joinees with self-service access to IT setup, tool access paths, HR policies, and common FAQs on day one.


WHAT LEADERSHIP GETS

- **AI-Assisted Plan Builder**: Generates structured 30-day onboarding drafts from a manager's brief in seconds, requiring human review before release.
- **Real-Time Progress Tracking**: Live dashboards tracking task completion, certifications, and key introductions without manual follow-up messages.
- **Compliance & Certification Guardrails**: Deadline tracking and proof-document uploads for mandatory regulatory certifications.
- **Self-Service Information Hub**: Seeded, categorized knowledge base resolving routine IT, tools, payroll, and workplace queries on day one.
- **Automated Due-Date Alerts**: Scheduled email reminders for approaching tasks and automated escalations to managers for overdue items.

HOW IT FITS TOGETHER

Manager Brief → AI Drafting Engine → Manager Review & Approval → Joinee Dashboard & Tracking → Progress & Escalation Engine

The architecture decouples AI drafting as an optional accelerator from the core application, ensuring all planning, tracking, and information hub workflows remain fully functional even during external provider outages.

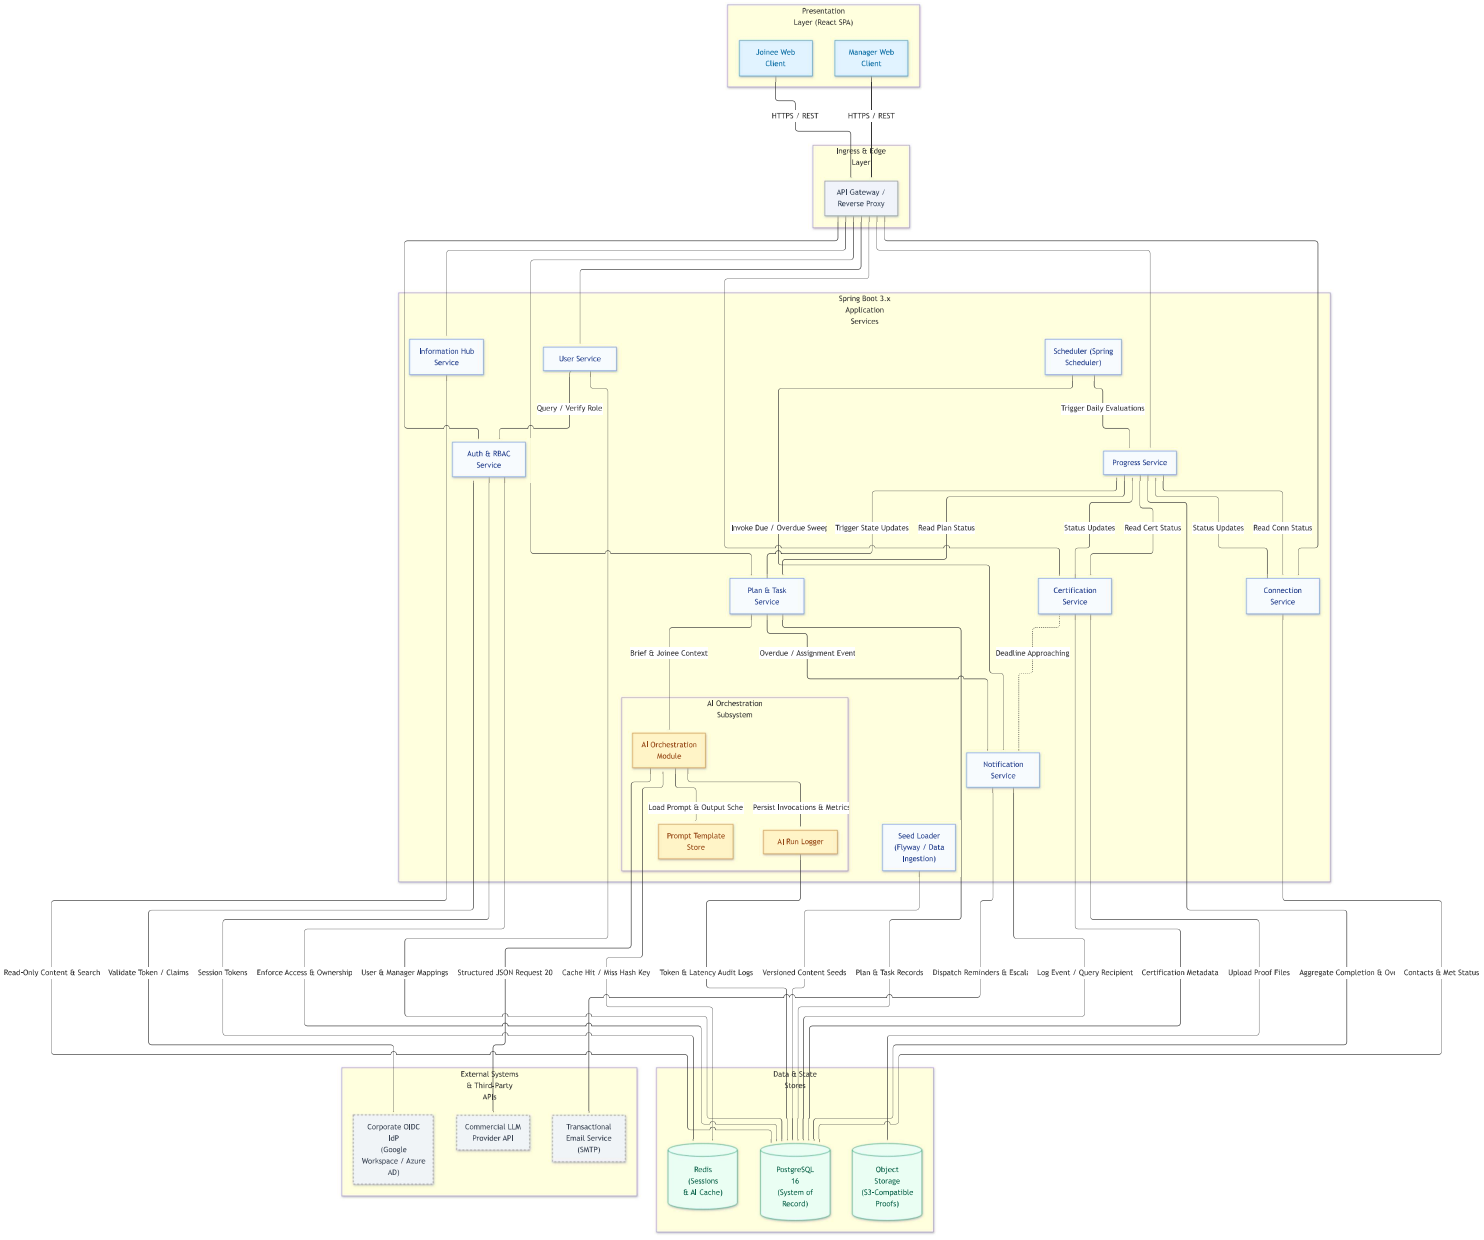

Architecture

QUESTIONS IT WILL ANSWER

- Which new hires have an active onboarding plan ready before their start date?
- Who is falling behind on mandatory compliance certifications and requires immediate escalation?

- How far along is each joinee across their 30-day onboarding milestones?
- Have all critical stakeholder introductory meetings been completed?
- How much manager time is saved per hire when creating onboarding plans?

WHAT IT DELIBERATELY EXCLUDES

- **AI-Generated People Recommendations**: Avoids fairness and org-chart accuracy issues; managers enter contacts directly.
- **AI Progress Summaries & Doc Q&A**: Avoids vector database costs and hallucination risks; deterministic dashboards and static hubs answer these cleanly.
- **AI-Suggested Certifications**: Excluded to prevent regulatory compliance risks from incorrect AI suggestions.
- **HRIS, Slack, and Calendar Integrations**: Deferred to keep initial release scope small and avoid external build dependencies.
- **Performance Appraisals and LMS Hosting**: Keeps focus strictly on onboarding workflow rather than duplicating core HR/LMS systems.

HOW WE WILL DELIVER IT

PHASE 0 — Discovery and Documentation

Finalise requirements, publish API contracts, secure InfoSec data boundaries, and collect signed-off Information Hub content.

PHASE 1 — Foundation

Implement OIDC authentication, database schema, manager-joinee role-based access, and deployment pipeline.

PHASE 2 — Information Hub

Deploy the seeded, searchable read-only knowledge base for IT, access, HR, and policy resources.

PHASE 3 — Manual Core

Deliver manual plan creation, task management, certification proof uploads, connection tracking, and progress dashboards.

PHASE 4 — AI Task Generation

Add prompt orchestration, schema validation, Redis response caching, and the manager draft-and-edit interface.

PHASE 5 — Notifications and Hardening

Implement scheduled reminders, overdue escalations, WCAG 2.1 AA accessibility compliance, and security hardening.

PHASE 6 — Pilot and Rollout

Run a live pilot with 2–3 managers, refine prompts based on real briefs, and launch to general availability.

Phases 2, 3, and 4 build sequentially upon the foundation delivered in Phase 1.

DECISIONS WE NEED FROM LEADERSHIP

Decision	Owner	Why it matters now
Approve data-boundary policy for non-PII context sent to LLM	Information Security	Unblocks AI service architecture and vendor integration.
Select and fund commercial LLM provider with monthly budget cap	Engineering Manager & Finance	Required before building AI orchestration and caching layers.
Designate named content owners for Information Hub categories	Head of HR & IT Operations Lead	Hub content must be seeded and signed off prior to Phase 2.
Confirm certification proof upload and retention requirements	Head of HR	Establishes storage configuration, retention schedules, and compliance policies.

RISKS WE ARE MANAGING OPENLY

- **AI generates inaccurate or generic tasks that managers approve without checking.**
  We enforce an editable review grid, require explicit approval actions, warn on unedited plans, and benchmark prompts against golden test suites.
- **Third-party LLM provider experiences outages, high latency, or throttling.**
  AI drafting operates with a hard 20-second timeout, one retry, and an immediate fallback to an

always-available manual creation flow.

- **Information Hub content becomes outdated and misleads new hires.**
  Every entry displays a visible last-reviewed date, assigns a named owner per category, and provides a joinee error-reporting action.
- **Cross-tenant data exposure between managers.**
  Authorisation checks are enforced strictly server-side on authenticated tokens, validated by automated cross-tenant test suites.

THE ASK

Approval from the Engineering Manager, Head of HR, IT Operations Lead, and Information Security reviewer to begin Phase 0 — Discovery and Documentation.
Completion of Phase 0 leads to a formal architecture and security review gate prior to committing build resources for Phase 1.

Full detail in BRD-EOD-001.
